EDGAR Online

MISSISSIPPI POWER CO

FORM 8-K
(Current report filing)

Filed 04/01/15 for the Period Ending 04/01/15

Address	2992 WEST BEACH GULFPORT, MS 39501
Telephone	2288641211
CIK	0000066904
Symbol	MPRWL
SIC Code	4911 - Electric Services
Industry	Electric Utilities
Sector	Utilities
Fiscal Year	12/31

Powered By EDGAR Online
http://www.edgar-online.com
© Copyright 2015, EDGAR Online, Inc. All Rights Reserved.
Distribution and use of this document restricted under EDGAR Online, Inc. Terms of Use.

UNITED STATES
SECURITIES AND EXCHANGE COMMISSION

Washington, D. C. 20549

FORM 8-K

CURRENT REPORT

Pursuant to Section 13 or 15(d) of the Securities Exchange Act of 1934

Date of Report (Date of earliest event reported) April 1, 2015

Commission File Number	**Registrant, State of Incorporation, Address and Telephone Number**	**I.R.S. Employer Identification No.**
001-11229	**Mississippi Power Company** (A Mississippi Corporation) 2992 West Beach Gulfport, Mississippi 39501 (228) 864-1211	64-0205820

The name and address of the registrant have not changed since the last report.

Check the appropriate box below if the Form 8-K filing is intended to simultaneously satisfy the filing obligation of the registrant under any of the following provisions:

[ ] Written communications pursuant to Rule 425 under the Securities Act (17 CFR 230.425)

[ ] Soliciting material pursuant to Rule 14a-12 under the Exchange Act (17 CFR 240.14a-12)

[ ] Pre-commencement communications pursuant to Rule 14d-2(b) under the Exchange Act (17 CFR 240.14d-2(b))

[ ] Pre-commencement communications pursuant to Rule 13e-4(c) under the Exchange Act (17 CFR 240.13e-4(c))

Item 7.01. Regulation FD Disclosure.

The information in this Current Report on Form 8-K, including the exhibit attached hereto, shall not be deemed "filed" for purposes of Section 18 of the Securities Exchange Act of 1934, as amended, or otherwise subject to the liabilities under that Section. Furthermore, such information, including the exhibit attached hereto, shall not be deemed to be incorporated by reference in any filing under the Securities Act of 1933, as amended, except as shall be expressly set forth by specific reference in such filing.

On April 1, 2015, Mississippi Power Company ("Mississippi Power") submitted its Kemper County Integrated Coal Gasification Combined Cycle Project Monthly Status Report through February 2015 (the "February PSC Report") to the Mississippi Public Service Commission (the "Mississippi PSC") pursuant to Docket No. 2009-UA-14. A copy of the February PSC Report is furnished as Exhibit 99.01 to this Current Report on Form 8-K.

Exhibit

Exhibit 99.01	Kemper County Integrated Coal Gasification Combined Cycle Project Monthly Status Report through February 2015 to the Mississippi Public Service Commission submitted by Mississippi Power Company pursuant to Docket No. 2009-UA-14.

Cautionary Note Regarding Forward-Looking Statements

Certain information contained in the February PSC Report is forward-looking information based on current expectations and plans that involve risks and uncertainties. Forward-looking information includes, among other things, statements concerning the projected cost and schedule for the completion of construction and start-up of the integrated coal gasification combined cycle project in Kemper County, Mississippi (the "Kemper IGCC"). Mississippi Power cautions that there are certain factors that could cause actual results to differ materially from the forward-looking information that has been provided. The reader is cautioned not to put undue reliance on this forward-looking information, which is not a guarantee of future performance and is subject to a number of uncertainties and other factors, many of which are outside the control of Mississippi Power; accordingly, there can be no assurance that such suggested results will be realized. The following factors, in

addition to those discussed in Mississippi Power's Annual Report on Form 10-K for the fiscal year ended December 31, 2014, and subsequent securities filings, could cause actual results to differ materially from management expectations as suggested by such forward-looking information: changes in tax and other laws and regulations to which Mississippi Power is subject as well as changes in application of existing laws and regulations; the ability to control costs and avoid cost overruns during the development and construction of facilities, which include the development and construction of generating facilities with designs that have not been finalized or previously constructed, including changes in labor costs and productivity, adverse weather conditions, shortages and inconsistent quality of equipment, materials, and labor, contractor or supplier delay, non-performance under construction or other agreements, operational readiness, including specialized operator training and required site safety programs, unforeseen engineering or design problems, start-up activities (including major equipment failure and system integration), and/or operational performance (including additional costs to satisfy any operational parameters ultimately adopted by the Mississippi PSC); the ability to construct facilities in accordance with the requirements of permits and licenses, to satisfy any environmental performance standards and the requirements of tax credits and other incentives, and to integrate facilities into the Southern Company system upon completion of construction; advances in technology; actions related to cost recovery for the Kemper IGCC, including actions relating to proposed securitization, Mississippi PSC approval of a rate recovery plan, including the ability to complete the proposed sale of an interest in the Kemper IGCC to South Mississippi Electric Power Association, the ability to utilize bonus depreciation, which currently requires that assets be placed in service in 2015, and satisfaction of requirements to utilize investment tax credits and grants; Mississippi PSC review of the prudence of Kemper IGCC costs; the ultimate outcome and impact of the February 2015 decision of the Mississippi Supreme Court, Mississippi Power's request for rehearing of such decision, and any further legal or regulatory proceedings regarding any settlement agreement between Mississippi Power and the Mississippi PSC, the March 2013 rate order regarding retail rate increases, or the State of Mississippi legislation designed to enhance the Mississippi PSC's authority to facilitate development and construction of baseload generation in the State of Mississippi; and the ability of counterparties of Mississippi Power to make payments as and when due and to perform as required. Mississippi Power expressly disclaims any obligation to update any forward-looking information.

SIGNATURE

Pursuant to the requirements of the Securities Exchange Act of 1934, the registrant has duly caused this report to be signed on its behalf by the undersigned hereunto duly authorized.

Date: April 1, 2015

MISSISSIPPI POWER COMPANY

By /s/Melissa K. Caen
Melissa K. Caen
Assistant Secretary

Mississippi Power
Kemper County IGCC Project

Table of Contents

MPSC Docket No. 2009-UA-0014
Monthly Status Report
Through February 2015

Project Costs and Summary	1
Key Contracts Over $10M	2
Project Updates	3
Safety	
Schedule	
Permits and Approvals	
Mississippi Economic Impact	4
Liberty Mine Summary	8

Table 1: Capped Plant Costs (in millions of dollars)

Cost Category	Current View	Variance from Previous Month	Actuals through February 2015	Confirmed Cost %
Land	$32.3	$0.0	$32.3	100%
EPC	4,108.3	4.4	3,932.5	96%
Transmission	94.2	0.0	94.0	100%
Fuel Facilities	153.3	(0.0)	141.4	91%
Pre Commercial Operations	494.4	(0.3)	322.5	52%
CC & Related Assets Placed in Service - Non-Incremental [1]	24.9	(0.1)	8.8	35%
Project Development	66.7	0.1	60.2	90%
Start Up Fuel / Energy	45.5	(0.0)	7.5	17%
DOE CCPI2 Funding	(245.3)	0.0	(245.3)	
Ad Valorem	24.8	0.0	23.7	95%
Schedule Risk	120.0	0.0	0.0	
Contingency	74.1	5.0	0.0	
Total Plant	4,993.3	9.0	4,377.6	
Deduction for Cap Exceptions (BC/FM/CIL)	(55.9)	0.0	(55.9)	
Total Plant Subject to Cost Cap	$4,937.4	$9.0	$4,321.7	91%

Table 2: Exemptions and Exceptions (in millions of dollars)

Cost Category	Current View	Variance from Previous Month	Actuals through February 2015
Mine *(details on p.8)* [2]	$232.3	$0.0	$232.3
CO2 Pipeline	108.5	(0.0)	92.0
Regulatory and Other Asset Accounts [3]	179.4	(0.6)	130.1
CC & Related Assets Placed in Service - Incremental (Net of Revenues) [4]	16.3	0.2	1.7
Project AFUDC - Non Mine [5]	629.9	(0.6)	470.0
Process Development Allowance	46.5	0.0	19.9
Beneficial Capital	47.6	0.0	47.6
Force Majeure	2.7	0.0	2.7
Change in Law	5.6	0.0	5.6
Total Exemptions and Exceptions	$1,268.8	($1.0)	$1,001.8

Table 3: Total Project Costs (in millions of dollars)

Cost Category	Current View
Total Plant Subject to Cost Cap [6]	$4,937.4
Total Exemptions and Exceptions	$1,268.8
Total Project Cost	$6,206.2
Amount in Excess of the Cost Cap	($2,057.4)
Total Amount Eligible for Recovery Under 2012 MPSC Order [7]	$4,148.8

(1) Non-incremental operating and maintenance costs related to the combined cycle and associated common facilities placed in service in August 2014 that are subject to the $2.88 billion cost cap.

(2) The Liberty Mine was placed in service in June 2013. Construction costs incurred since that date are reported above as Mine costs. Operational costs incurred since the mine was placed in service are not included in this report. These costs are considered to be post-COD capital and fuel inventory costs and will be subject to MPUS and MPSC oversight in conjunction with the annual review of fuel costs.

(3) The debt carrying cost associated with assets placed in service and other non-construction work in progress accounts are being deferred and are included in regulatory assets. The equity return associated with assets placed in service and other non-construction work in progress accounts are not included in this report.

(4) Incremental operating and maintenance costs related to the combined cycle and associated common facilities placed in service in August 2014. This amount includes a credit for variable operating and maintenance expenses related to energy sales, net of station service.

(5) AFUDC related to the combined cycle and associated common facilities placed in service ceased in August 2014.

(6) Mississippi Power Company has revised its cost estimate subject to the cost cap for the Kemper IGCC to include approximately $9 million in cost increases primarily related to additional labor costs in support of start-up and operational readiness activities.

(7) Total Amount Eligible for Recovery under 2012 MPSC Order is net of the Company's estimated loss as a result of exceeding the cost cap of $2.88 billion. This amount includes estimated costs through March 31, 2016, is based on information available through the filing date, and is subject to review and approval by the MPSC.

Major Items and Milestones Achieved

- The purchase of 2,968 acres for the plant site has been completed.
- Construction is complete for the nitrogen plant, water plant, water storage lake, administrative and electrical buildings, lignite storage dome, electrical ductbanks, concrete installation, structural steel, process piping installation, cable tray, tubing, and underground piping.
- The combined cycle was placed in service on natural gas on August 9, 2014.
- Construction is complete on the three 115kV line rebuild projects. The four new 230kV lines, one new 115kV line, and the mine service line are complete and energized. Construction is complete on eight substations and the Sweatt - Sykes fiber line.
- The treated effluent, natural gas, and CO_2 pipeline installations are 100% complete. Closeout activities remain on all three pipelines.
- Long term contracts have been signed for the sale of CO_2, sulfuric acid, and ammonia.
- Subject to Commission approval and the completion of several milestones, SMEPA will have a 15% ownership interest in the Project.
- First Fire Gasifier "B" achieved on March 1, 2015 and First Fire Gasifier "A" achieved on March 2, 2015

Mississippi Economic Impact

- Mississippi workforce contributed 488 construction jobs in February for the Project. A total of 524 Mississippi companies have provided construction, equipment, material or professional services for the Project.

Overall Project Status

- Mississippi Power placed the combined cycle unit and associated common facilities portion of the Kemper IGCC in service on August 9, 2014. The remainder of the Kemper IGCC is expected to be placed in service in the first half of 2016.

Table 4: Key Contracts Over $10M

(in millions of dollars)	Issue Initial Inquiry	Award Date	Current View	Variance from Previous Month
Equipment and Material Contracts Over $10M *(Represents 92% of total equipment and material contracts)*	Dates in BOLD are actual dates; others are forecast dates		$1,486.7	$0.2
Steam Turbine Generator	**Nov-07**	**Aug-08**		
Gas Turbines	**Dec-08**	**Aug-09**		
Heat Recovery Steam Generators	**Oct-09**	**Jun-10**		
Syngas Coolers	**Jan-10**	**May-10**		
Transport Gasifiers	**Jan-10**	**May-10**		
Fluid Bed Dryers	**Mar-10**	**Jul-10**		
Air Compressors	**Apr-10**	**Sep-10**		
Nitrogen Generation System	**Jun-10**	**Dec-10**		
Particulate Control Device (PCD) Systems	**Nov-10**	**Sep-11**		
Generator Step-up Transformers	**Jul-10**	**Jan-11**		
Station Service Transformers	**Jul-10**	**Dec-10**		
Coal Dense Phase Conveyors	**Sep-10**	**Nov-10**		
Coal Lock Vessels	**Aug-10**	**Jan-11**		
Water Treatment System	**Jul-10**	**Feb-11**		
Structural Steel	**Sep-10**	**Dec-10**		
Heat Exchangers	**Apr-10**	Multiple		
Chemical Reactors	**Jul-10**	Multiple		
Vessels	**Jun-10**	Multiple		
Heat Exchangers	**Jul-10**	Multiple		
Compressors	**Jun-10**	Multiple		
Catalyst	**Jul-10**	Multiple		
Pumps	**Jun-10**	Multiple		
Drums	**Jan-10**	Multiple		
Unit Chillers	**Jul-10**	Multiple		
Construction Piping	**Jun-10**	Multiple		
Instrumentation & Controls	**Oct-10**	Multiple		
Electrical	**Apr-11**	Multiple		
Transmission Line Structures	**May-11**	Multiple		
Construction Contracts Over $10M *(Represents 99% of total construction contracts)*	Dates in BOLD are actual dates; others are forecast dates		$1,880.6	$0.9
Cut and Fill Excavation	**Jul-10**	**Aug-10**		
Underground	**Nov-10**	**Jan-11**		
Concrete	**Nov-10**	**Jan-11**		
Gasifier General Contractor	**Apr-11**	**Jul-11**		
Combined Cycle General Contractor	**Oct-11**	**Dec-11**		
Water Lateral	**Jul-11**	**Sep-11**		
Architectural Buildings	**Feb-11**	Multiple		
Cooling Tower	**Feb-10**	**Sep-10**		
Insulation	**Jan-12**	**Jun-12**		
Field Erected Tanks	**Nov-10**	**Feb-11**		
Water Storage Pond	**Nov-11**	**Dec-11**		
Gas Clean-up & By Products	**Oct-11**	**Dec-11**		
Turbine Generator	**Nov-11**	**Dec-11**		
HRSG Erection	**Aug-11**	**Sep-11**		
Piling	**Sep-10**	**Dec-10**		
Ash Storage	**Nov-11**	**Dec-11**		
Total			$3,367.3	$1.1

Safety

OSHA Recordable Incident Rate:	Project to Date:	.48	Work Hours:	Project to Date:	32,757,491
	Year to Date:	.00		Year to Date:	860,592

Schedule - Key 90-Day Milestones

	Forecast	Actual	Comments
First Fire Gasifier A	Mar-15	Mar-15	
First Fire Gasifier B	Mar-15	Mar-15	
Air Flow Testing Complete - Train A	Apr-15		Previously forecasted in May15
Air Flow Testing Complete - Train B	Apr-15		Previously forecasted in May15
Fluidization Trial - Train A	May-15		

Schedule - Overall Project

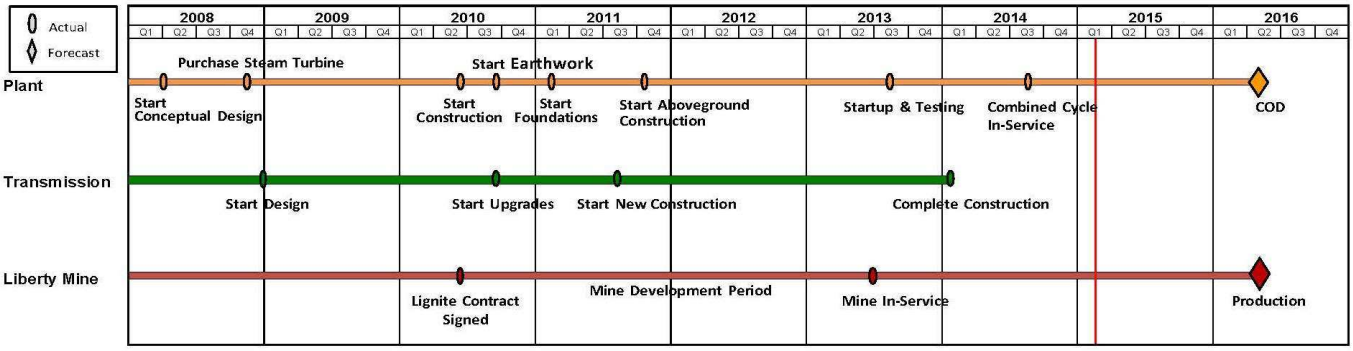

Permits and Approvals

Dates in **Bold** are actual dates, others are forecast dates

Description	Status	Submittal	Approval
State Groundwater Test Well Permit MS-GW-16425	Approved	**5/30/07**	**6/26/07**
State NPDES Stormwater Run-off Permit MSR104866	Approved	**11/13/07**	**3/12/10**
State PSD Air Permit 1380-00017	Approved	**12/20/07**	**3/12/10**
State Groundwater Production Well Permit MS-GW-16562	Approved	**5/21/08**	**7/22/08**
MPSC Certificate	Approved	**1/16/09**	**6/3/10**
State Permit to Operate Wastewater Disposal System w/no Discharge Permit MSU009005 (1)	Approved	**11/19/09**	**3/12/10**
State Dam Safety Approval App. No. 09-041	Approved	**12/1/09**	**3/23/10**
State Dam Safety Approval App. No. 09-040	Approved	**12/1/09**	**3/23/10**
FAA stack permit	Approved	**2/8/11**	**3/14/11**
DOE NEPA ROD (CCPI2)	Approved	**11/6/09**	**8/19/10**
State 401 Water Quality Certification	Approved	**10/27/09**	**9/14/10**
USACE 404 Permit for Wetlands SAM-2009-01149-DMY	Approved	**10/27/09**	**11/18/10**
State Solid Waste Management Permit	Approved	**6/11/10**	**11/15/11**
State Dam Safety - Make-up Reservoir	Approved	**6/3/11**	**8/12/11**
State Dam Safety - Retention Pond B	Approved	**6/1/11**	**8/9/11**
Dam Safety LDF Retention Pond Permit	Approved	**10/6/11**	**11/2/11**
NPDES Emergency Discharge Permit	Approved	**12/1/11**	**8/12/14**
NPDES Baseline Industrial Storm Water General Permit	Approved	**5/24/13**	**3/7/14**
Title IV Acid Rain Permit	Pending	**10/13/11**	
Title V Operating Permit	Pending	**8/22/14**	

(1) State Permit to Operate Wastewater Disposal System w/no Discharge Permit MSU009005 was revoked on 8/12/14 due to the approval of the NPDES Emergency Discharge Permit on 8/12/14.

Economic Impact

Table 5: Mississippi Construction, Equipment, Material and Professional Services Companies (Tier 1)

Company Name	City	Type of Work
3 D Trucking	Louisville	Professional Service
3point Technologies	Columbus	Professional Service
4 County Electric Power Association	Columbus	Construction
A E Allen	Pass Christian	Construction
A&B Electric	Meridian	Professional Services
AA Calibration Services	Yazoo City	Professional Service
ABF Freight	Jackson	Material
Accu-Fab & Construction, Inc	Moss Point	Material
ADCO Companies Ltd	Brandon	Equipment
AES Limited PC	Meridian	Construction
Aggreko Cooling Tower Service	Ridgeland	Equipment
Air Center of Mississippi	Jackson	Material
Air Management, LLC	Meridian	Construction
Air Tool Supply	West Point	Material
Airgas South	Meridian	Construction
AJA Management	Jackson	Professional Services
Al Covington / Bill Oubre	Meridian	Construction
All Brand Foods	Hattiesburg	Professional Services
All Clean Janitorial	DeKalb	Professional Services
All Safe Technologies	Gulfport	Professional Services
All Star Printing	Columbus	Materials
Almetek Industries Inc	Ridgeland	Material
American Controls	Amory	Material
American Fire & Safety	Laurel	Professional Services
American Forest Management	Meridian	Professional Services
American Rental	Philadelphia	Construction
American Supply Co Inc	Jackson	Material
Anderson Retail	Hattiesburg	Material
APAC Mississippi Inc	Jackson	Construction
Appraisal Group	Philadelphia	Professional Services
Appraisers Associated Ltd.	Meridian	Professional Services
Aquaterra Engineering LLC	Madison	Professional Services
Argus Analytical	Jackson	Professional Services
Asplundh Tree Expert Co	D'Iberville	Construction
Atwood Fence	Kosciusko	Construction
B Clean	Laurel	Professional Services
Baker Ready Mix	Louisville	Material
Balch & Bingham, LLP	Gulfport	Professional Services
Barnhart Crane & Rigging	Jackson	Construction
Bay Pest Control	Ocean Springs	Professional Services
Bayou Management Inc	Columbus	Professional Services
Bellavilla Community Club	Bailey	Construction
Bengal Resources and Associates, Inc.	Columbia	Professional Services
Betty Luke	Bailey	Professional Services
Bill Oakley Consulting Hydrologist, Inc.	Brandon	Professional Services
Bill's Trailer Sales	Ackerman	Materials
Black Brothers, Inc.	Ackerman	Construction
Blackwell Shepards Locksmith	Meridian	Professional Services
Blaine's Trailer Rental & Sale	Richland	Construction
BMI Environmental Services	Gulfport	Professional Services
Bonds of Love Ministries	DeKalb	Construction
Briggs Equipment	Jackson	Construction
Broadmoor Home	Meridian	Construction
Brown Printing Company	Meridian	Construction
Brown & Mitchell	Gulfport	Construction
Brunini	Jackson	Professional Services
Buckwalter Stadium Inc.	Meridian	Construction
Burford Electric Service, Inc	Columbus	Construction
Burkhalter Rigging Inc	Columbus	Construction
Burk's Aviation	Hattiesburg	Professional Services
Business Interiors	Jackson	Professional Services
Can't Be Beat Fencing	Perkinston	Construction
Capital Concrete Cutting Inc	Clinton	Materials
Capitol Hardware Company, Inc.	Jackson	Professional Services
Carter Miller Associates	Meridian	Professional Services
Cavco, Inc	Bailey	Construction
Central Culvert & Pipe	Philadelphia	Material
Central Mississippi Communications	Kosciusko	Professional Services
Central Office Supply	Kosciusko	Construction
Central Pipe Supply Inc	Jackson	Material
Chain Electric Co.	Hattiesburg	Construction
Chancellor Supply	Laurel	Material
Chet's Paint & Body Shop	Meridian	Professional Services
Chevron Products	Moss Point	Equipment
Chris Haynes Electric Supply	Jackson	Materials
Cintas Corporation	Jackson	Construction
Cintas FAS	Jackson	Professional Services
City of Meridian	Meridian	Professional Services
Cives Steel Co.	Rosedale	Material
Collins and Null	Hattiesburg	Professional Services
Collinsville Hardware	Meridian	Material
Columbus Rubber & Gasket	Columbus	Construction
Commercial Interiors	Long Beach	Professional Services
Comsouth	Meridian	Professional Services
Consolidated Electrical Distributors Inc	Gulfport	Material
Consolidated Pipe & Supply Co	Pascagoula	Material
Contract Fabricators, Inc.	Holly Springs	Equipment
Cornett Bolt & Screw	Gulfport	Material
CSS Document Solutions	Meridian	Professional Services
CTC, Inc	Louisville	Material
Cuevas Auction, LLC	Picayune	Professional Services
Custom Creations and More	Meridian	Construction
D&E Construction Co Inc	Meridian	Construction
DACO LLC	Columbus	Professional Services
Daily Equipment Co Inc	Jackson	Construction
David L. Moon	Collinsville	Construction
Davidson Hauling & Constriction	Marion	Material
Davis Trailer	Moselle	Construction
Deep South Services LLC	Hickory	Material
Design Precast and Pipe	Gulfport	Construction
Dickerson Petroleum	Kosciusko	Construction
Ditch Witch of Mississippi	Pearl	Construction
Dixie Mat & Hardwood Co Inc	Sandy Hook	Material
Doug Jones & Son Construction Co	Meridian	Construction
Douglas Inc.	Jackson	Professional Service
Dowdle Gas Company	DeKalb	Construction
Dr. David Lang, PhD	Starkville	Professional Services
DZ Atlantic	Moss Point	Equipment
E. Patrick Cassady & Associates Inc.	Gulfport	Professional Services
Earl Dudley Associated	Jackson	Construction

continued on page 5

Economic Impact *(continued from page 4)*

Table 5: *(continued)* **Mississippi Construction, Equipment, Material and Professional Services Companies (Tier 1)**

Company Name	City	Type of Work	Company Name	City	Type of Work
East Mississippi Electric Power Assoc.	Meridian	Construction	Hi Grade Gin Corporation	Winona	Construction
ECO Systems (now Allen Eng. & Science)	Jackson	Professional Services	HJM Forest Resource Management	DeKalb	Professional Services
Eddie Briggs, Attorney at Law	Madison	Professional Services	Holliday Construction	Poplarville	Construction
Educational Furniture & Equipment Co.	Meridian	Construction	Holloway Termite & Pest Services	Meridian	Professional Services
Eley Guild Hardy Architects	Biloxi	Professional Services	Hooper Electronics	Pascagoula	Material
Endom Welding & Trailer Repair	Ellisville	Construction	Hotel & Restaurant Supply	Meridian	Material
Engineering Plus	Meridian	Professional Services	Howard Industries	Laurel	Equipment
Engineering Services	Jackson	Professional Services	HRD Safety	Jackson	Material
Eutaw Construction	Aberdeen	Construction	Hughes Brothers Inc	Jackson	Material
F L Clayton Trust	Meridian	Construction	Ice Plant	Meridian	Construction
Faison Office Products Co LLC	Gulfport	Construction	Industrial Commercial Fire Protection	Lucedale	Construction
Fastenal	Philadelphia	Material	Industrial Electric Motor Works Inc	Meridian	Professional Services
FC&E Engineering LLC	Brandon	Professional Services	Industrial Machine & Manufacturing	Meridian	Professional Services
Ferguson Enterprises	Jackson	Equipment	Industrial Steel Corp.	Jackson	Construction
Firestone	Meridian	Professional Services	Infolab, LLC	Clarksdale	Professional Services
Fish and Fisher	Jackson	Construction	Ivy Consulting	Quitman	Professional Services
Fluid Process & Pumps	Florence	Material	J & J Contractors	Collinsville	Professional Services
Forest Services, Inc.	Pelahatchie	Professional Services	J W Lee Company, Inc	Gulfport	Equipment
Forestry Suppliers	Brandon	Construction	Jabez Group, LLC	Madison	Professional Services
Fraley Dozer Service	Collins	Construction	Jackson Bolt & Screw	Jackson	Material
Fulton Line Service	Preston	Construction	James Self Inc dba JSI Communication	Pearl	Material
G & K Services	Jackson	Professional Services	JH Haynes Electric Co Inc	Gulfport	Professional Services
G & O Supply Co. Inc.	Houston	Material	Joe McGee Construction	Lake	Construction
Gary G. Williams, Appraisals	Flowood	Professional Services	John B. Stewart Real Estate Appraiser	Canton	Professional Services
Genesis Telecommunications	Collinsville	Professional Services	John C Stennis Memorial Hospital	DeKalb	Professional Services
GEO Products	Madison	Material	John Fayard Moving & Warehousing, LLC	Gulfport	Materials
George's Auto Parts	Meridian	Construction	John's Welding	Meridian	Professional Services
Geotechnical Engineering Assoc.	Ridgeland	Professional Services	Johnson Surveying	Collinsville	Professional Services
Gipson Steel Inc	Meridian	Construction	K. C. Garbage & Solid Waste	DeKalb	Construction
Glass Inc.	Meridian	Material	Kelly Services	Gulfport	Professional Services
Glassworx	Philadelphia	Material	Kemper Construction Supply	DeKalb	Material
Glenn Hollingsworth Enterprise LLC	Hickory	Construction	Kemper County Landfill	DeKalb	Professional Services
Glenn Machine Works	Columbus	Construction	Kemper County Messenger	DeKalb	Professional Services
Glover Young Walton & Simmons, PLLC	Meridian	Professional Services	Kemper Electric Supply	DeKalb	Material
Godwin Group	Jackson	Professional Services	Kennedy Construction	Meridian	Construction
Goforth Forest Management, Inc.	Meridian	Professional Services	Knesal Engineering Services, Inc.	Gulfport	Professional Services
GraRock Trucking	Macon	Construction	Knowles Material Co	Jackson	Material
Greenway Construction	Wiggins	Construction	L & M Carpet Cleaning	Meridian	Professional Services
Gulf Coast Fence	Pascagoula	Construction	Lauderdale County Farm Supply	Meridian	Materials
Gulf Office Systems Inc	Saucier	Professional Services	Laurel Ford	Laurel	Equipment
Gulf Sales & Supply	Pascagoula	Construction	Lawyers PLLC	Meridian	Professional Services
Gulf South Survey & Environmental	Biloxi	Professional Services	Layne Christenson	Jackson	Construction
H & H Chief Sales	Carthage	Construction	LPK Architects	Meridian	Professional Services
H & H Construction	Greenwood	Construction	Luke Printing Company	Meridian	Professional Services
H & P Leasing, Inc.	Flowood	Construction	Lyle Machinery Company	Jackson	Equipment
Hampton & Associates Law Office	DeKalb	Professional Services	M G Dyess Inc	Bassfield	Construction
Hanson	Gulfport	Construction	M&M Holdings	Kilmichael	Materials
Hargrove Engineers Constructors	Pascagoula	Professional Services	Magnolia Steel Co, Inc.	Meridian	Professional Services
Havard Pest Control	Hattiesburg	Professional Services	Mailroom Consultants	Jackson	Professional Services
HD Supply Waterworks LTD	Pearl	Material	Malouf	Greenwood	Construction
Heartland Pump Rental & Sales Inc	Horn Lake	Construction	Mar-Com Comm, Inc.	Decatur	Construction
Heblon Heating & Air Conditioning	Meridian	Construction	Marion Water Department	Marion	Construction
Hemphill Construction	Florence	Construction	Mars Manufactured Homes	Meridian	Construction
Henderson Steel Corp	Marion	Construction	Martin Supply (MISCO)	Saltillo	Materials
Herring Gas Co Inc.	Philadelphia	Construction	Martin Truck & Tractor	Columbus	Construction

continued on page 6

Economic Impact *(continued from page 5)*

Table 5: *(continued)* Mississippi Construction, Equipment, Material and Professional Services Companies (Tier 1)

Company Name	City	Type of Work
Marvin's	Meridian	Material
Mary Joyce Angero	Meridian	Construction
Max Floor Specialist	Brandon	Professional Services
McCrary Construction Services	Columbus	Construction
McElroy Plumbing & Heating	Meridian	Construction
Medical Foundation (Rush Hospital)	Meridian	Professional Services
MEI Electrical Inc	Philadelphia	Construction
Melvin Chaney Jr Real Estate Appraiser	Madison	Professional Services
Mercury Aviation Inc	Flowood	Professional Services
Meridian Community College	Meridian	Professional Services
Meridian Personnel Service	Meridian	Professional Services
Meridian Tire & Brake	Meridian	Professional Services
Micro Methods Laboratory Inc	Ocean Springs	Professional Services
Mid South Welding	Meridian	Construction
Mikropul	Iuka	Equipment
Miller Enterprises	Hattiesburg	Construction
MillerCo Inc.	Gulfport	Construction
Milton's A/C Service	DeKalb	Construction
Mississippi Beverage Water, LLC	Meridian	Construction
Mississippi Department of Transportation	Jackson	Construction
Mississippi Gauge & Supply, Inc.	Meridian	Materials
Mississippi State University	Starkville	Professional Services
Missouth Vital Records	Meridian	Professional Services
Mitchell Sign, Inc.	Meridian	Professional Services
MMC Material	Meridian	Construction
Modern Landscape Design	Meridian	Professional Services
Modular Space Corp	Jackson	Construction
Motion Industries	Meridian	Materials
Mowdy Cabinetry	Meridian	Professional Services
MSC Industrial	Meridian	Materials
Necaise Locksmith Service	Gulfport	Materials
Neel Schaffer	Jackson	Professional Services
Nehring	Ridgeland	Material
Newell Paper Company	Meridian	Materials
NGK Locke Inc	Ridgeland	Material
NL Carson	Carthage	Construction
North Mississippi Medical Center	Eupora	Professional Services
Northwest Kemper Water Association	Preston	Construction
Office Furniture Jackson CIN	Ridgeland	Construction
Office Innovations	Ridgeland	Construction
ORR Safety Corp	Jackson	Material
Pac Services	Biloxi	Professional Services
Pearson Services	Louisville	Construction
Perfect Touch Contractors LLC	DeKalb	Construction
Perma R Products	Grenada	Material
Peterbilt Truck Center	Jackson	Construction
Pettigrew Forestry Consultants	Kiln	Professional Services
Pickering & Associates	Jackson	Professional Services
Plan House Printing and Graphics	Tupelo	Professional Services
Powell Transportation	Columbia	Material
Preformed Line Products Co	Ridgeland	Material
Print Plus	Meridian	Professional Services
Pritchard Engineering	Starkville	Professional Services
Pro Turf, Inc.	Winona	Construction
Procall Services	Biloxi	Professional Services
Progressive Pipeline	Meridian	Construction
ProModular	Jackson	Construction
Provine Helicopter Service, Inc.	Greenwood	Professional Services
Puckett Machinery Co	Jackson	Construction
Puckett Rents Inc	Jackson	Construction
Quality Welding & Fabrication	Columbia	Equipment
Ralph L. Morgan	Meridian	Material
Richard R. Hite Appraisal, LLC	Canton	Professional Services
Robert's Sewing Machine Parts	Meridian	Professional Services
Robinson Electric Supply Co Inc	Meridian	Material
Roto-Rooter Sewer & Drain	Meridian	Professional Services
RMKPC, Inc dba Orkin	Meridian	Professional Services
Robine & Welch Machine & Tool Co.	Laurel	Construction
Rush Care	Meridian	Professional Services
Ryan Motors Inc	Hattiesburg	Construction
S&S Welding	Ellisville	Professional Services
Sam Oswalt & Son, Inc.	Starkville	Construction
Sanders Air & Heat	Meridian	Professional Services
Sanders Gas	Meridian	Construction
Sequel Electrical Supply	Meridian	Material
Service Master	Marion	Professional Services
Sherwin Williams	Meridian	Material
Sign's Plus of Meridian	Meridian	Construction
Singley Construction Co	Columbia	Construction
Sirmon & Associates	Pelahatchie	Professional Services
Slay Steel Inc	Meridian	Material
South Mississippi Hydroseeding	Wiggins	Construction
Southern Business Supply	Meridian	Construction
Southern Chevrolet	DeKalb	Construction
Southern Colonel Homes Inc	Hattiesburg	Construction
Southern Natural Resources, Inc.	Stewart	Professional Services
Southern Pine Electric	Taylorsville	Equipment
Southern Pipe & Supply Co Inc	Gulfport	Material
Southern Surveyors Group LLC	Gulfport	Professional Services
Southern Tire Mart	Meridian	Construction
Southern Waste Disposal	Meridian	Construction
SPCS Inc	Gulfport	Professional Services
Specialty Fencing	Meridian	Construction
Specialty Fuel	Kosciusko	Construction
Starkville Computers	Starkville	Construction
Stevie Holiday	DeKalb	Professional Services
Stewart Environmental Construction	Tupelo	Construction
Stribling Equipment	Jackson	Construction
Strickland Companies	Columbus	Construction
Structural Steel Services	Meridian	Material
Stuart C. Irby Co.	Meridian/Jackson	Material
Sturgis Mat	Ackerman	Material
Sudden Service	Louisville	Construction
Sunbelt Equipment Marketing	Meridian	Construction
Sunbelt Insulation	Lucedale	Material
Sutton Lumber	Meridian	Material
Suzy Q Monogramming Screenprinting	Philadelphia	Construction
Swetman Security Service, Inc	Biloxi	Professional Services
System Scale	Jackson	Equipment
T K Stanley	Waynesboro	Material

continued on page 7

Economic Impact *(continued from page 6)*

Table 5: *(continued)* Mississippi Construction, Equipment, Material and Professional Services Companies (Tier 1)

Company Name	City	Type of Work	Company Name	City	Type of Work
Taylor Machine Works	Louisville	Construction			
Tencarva Machinery	Jackson	Construction			
Terracon Consultants	Madison	Professional Services			
The 1869 Group LLC	Jackson	Construction			
The Bolt Co dba Henderson Bolt	Meridian	Material			
The McGinnis Lumber Company	Meridian	Material			
The Service Company of Mississippi	Meridian	Professional Services			
Thomas Refrigeration	Meridian	Professional Services			
Threaded Fasteners	Gulfport	Material			
Thomasson Company	Philadelphia	Construction			
Tice Engineering	Wiggins	Professional Services			
Tim Parker Construction	Soso	Construction			
Timber Craft, Inc.	DeKalb	Professional Services			
Tolbert Chevrolet	Philadelphia	Construction			
Tooney's Tire Center	DeKalb	Professional Services			
Town of DeKalb	DeKalb	Construction			
Town of Marion	Marion	Construction			
Tri-State Consulting Services	Philadelphia	Professional Services			
Truckers Supply	Meridian	Construction			
TST&E, LLC	Carriere	Construction			
Tull Brothers	Meridian	Construction			
U Save Car & Truck Rental	Meridian	Construction			
Underwood Sales Inc	Ovett	Construction			
United Fence	Meridian	Construction			
United Rentals N.A. (formally RSC Eqmt)	Meridian	Construction			
Vice Brothers Unlimited	Moss Point	Material			
Vice Construction Co.	Moss Point	Construction			
Vick's Paint & Body Shop	DeKalb	Professional Services			
Volvo Rents	Hattiesburg	Construction			
Vulcan	Laurel	Material			
W G Yates & Sons Construction	Biloxi	Construction			
W.L. Cook	Bailey	Professional Services			
Walker Audio	Biloxi	Professional Services			
Walley Forestry	Ellisville	Professional Services			
Waring Oil Company LLC	Vicksburg	Material			
Waste Management	Tupelo & Meridian	Professional Services			
Waste Pro of MS	Meridian	Professional Services			
Waters International	Meridian	Material			
Waters Truck & Tractor	Kosciusko	Construction			
Waterstone Business Strategies	Brandon	Professional Services			
Watson Quality Ford	Jackson	Construction			
Watt Equipment	DeKalb	Construction			
Wilkerson Construction	DeKalb	Construction			
William Clay	DeKalb	Construction			
Woodall Electric Inc	Meridian	Professional Services			
Woodstock Furniture	Meridian	Construction			
Working Solutions	Meridian	Professional Services			
Yard Services	Meridian	Professional Services			

Total Mississippi Contracts - Tier 1 and Tier 2 (in millions of dollars)	**$1,464**
Total Mississippi Spend through February 2015 - Tier 1 and Tier 2 (in millions of dollars)	**$1,447**

Mississippi Workforce	Plant	Mine	Total
Construction Jobs	**488**	**0**	**488**
Plant/Mine Jobs	**178**	**117**	**295**

Mine Status

The surface coal mining and water pollution control permits for the Liberty Mine were approved by the MDEQ Permit Board on December 13, 2011. Liberty Mine began commercial operations on June 5, 2013. The dragline was placed in service on November 15, 2013. Construction activities are complete for the mine.

Table 6: Mine Costs (in millions of dollars)

Cost Category	Current View	Actuals through February 2015
Development	$80.0	$80.0
Land and Mineral Leases	29.5	29.5
Equipment	106.3	106.3
Mine AFUDC	16.5	16.5
TOTAL [1]	$232.3	$232.3

(1) The Liberty Mine was placed in service in June 2013. Construction costs incurred since that date are reported above as Mine costs. Operational costs incurred since the mine was placed in service are not included in this report. These costs are considered to be post-COD capital and fuel inventory costs and will be subject to MPUS and MPSC oversight in conjunction with the annual review of fuel costs.

Mine Safety

Recordable Incident Rate: 1.08

Project to Date Work Hours: 925,492

Mine Permits and Approvals

Dates in **Bold** are actual dates, others are forecast dates

Description	Status	Submittal	Approval
401 Water Quality Certification	Approved	**8/9/10**	**9/14/10**
404 USCAE Permit	Approved	**8/9/10**	**12/10/10**
MSHA Sedimentation Pond (Revision to include pond)	Approved	**8/29/13**	**6/23/14**
MSHA Mine Identification Number	Approved	**12/7/10**	**12/8/10**
State mine permit (SMCRA)	Approved	**1/18/11**	**12/14/11**
NPDES permit	Approved	**3/1/11**	**12/14/11**
State Dam Construction Permit	Approved	**3/18/11**	**6/29/11**
State Stormwater Permit	Approved	**11/23/11**	**1/27/12**
SPCC Plan	Approved	**3/30/12**	**3/30/12**
State Wastewater Discharge (Sewage)	*Not required; zero discharge system planned*		
Dragline FAA permit	Approved	**7/9/12**	**8/13/12**
